Montclair/Four Seasons Water System Improvements Design-Build Project

Four Seasons at Historic Virginia Annual Meeting May 17, 2023

Service Authority:David ScottProject ManagerProject Rep: ArcadisChris RemmeArea ManagerMike EarlyConstruction ManagerDesign-Builder:ACE/KCIKayla MatisProject Manager







Agenda

- Site Layouts
- Architectural Renderings
- Recent Construction Photos and Video
- Project Schedule and Status Update
- Service Authority (SA) Commitments
- Q&A





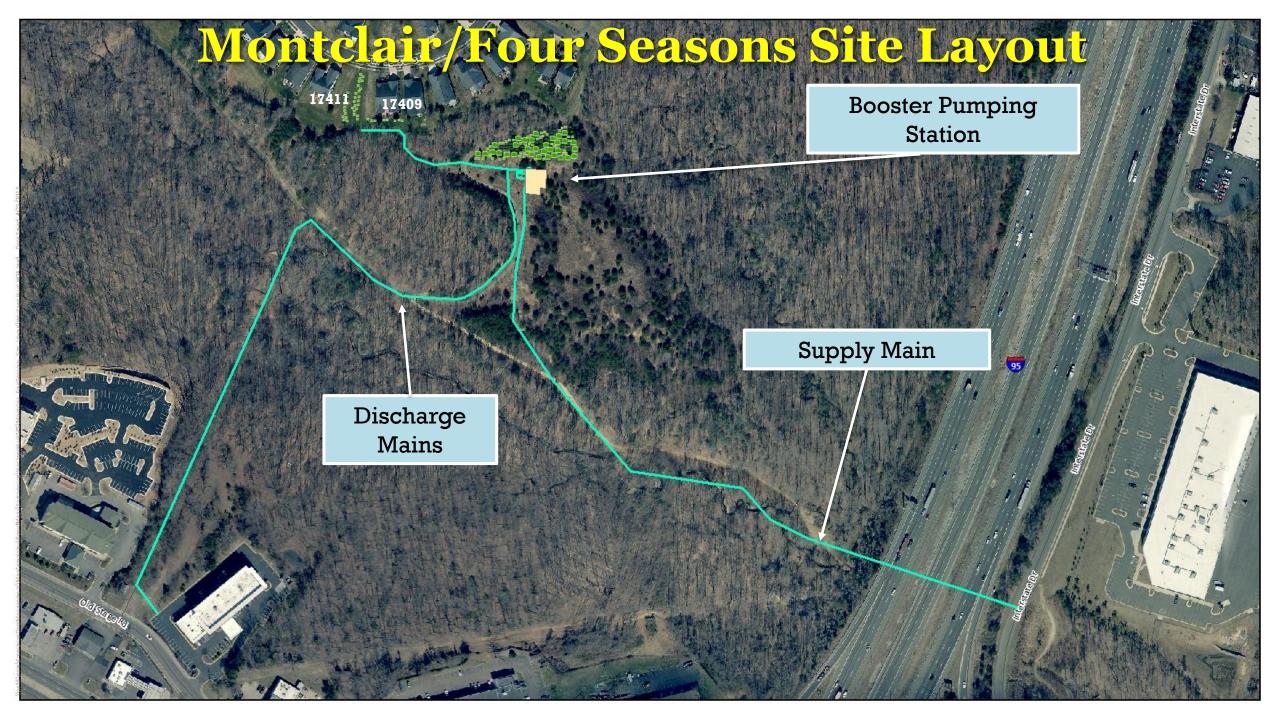

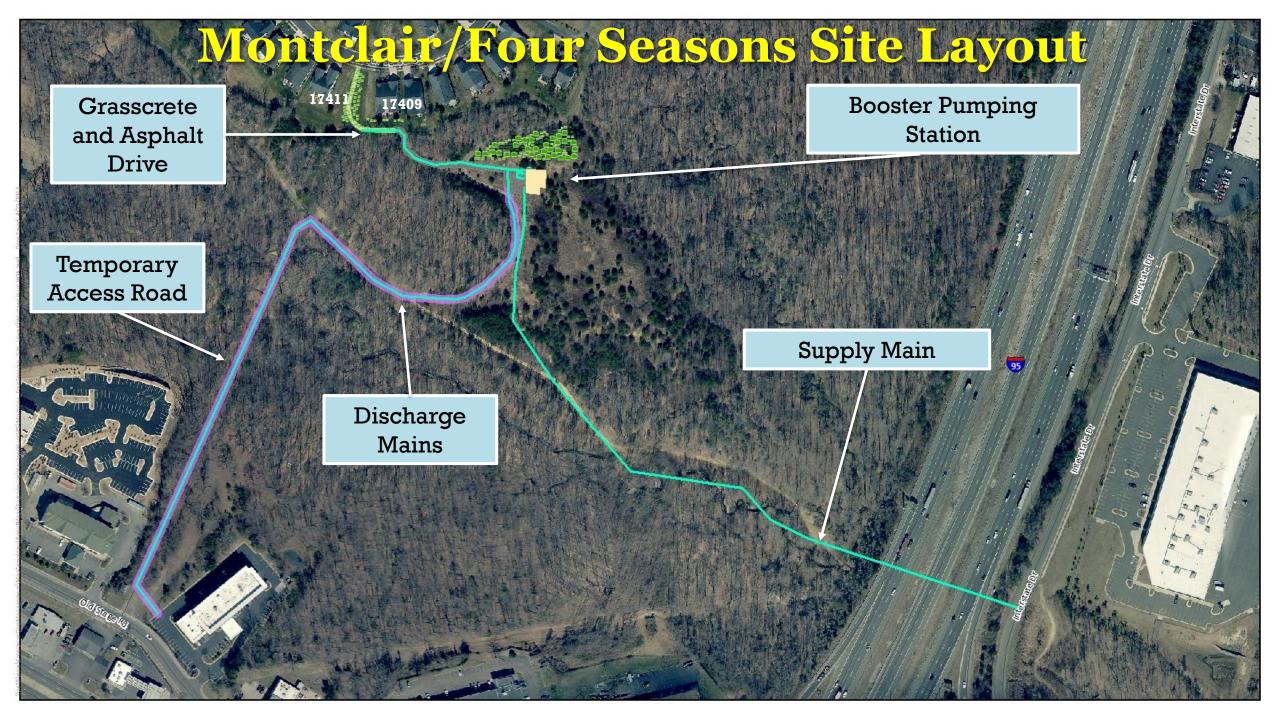





VIEW










Temporary Access Road from Old Stage

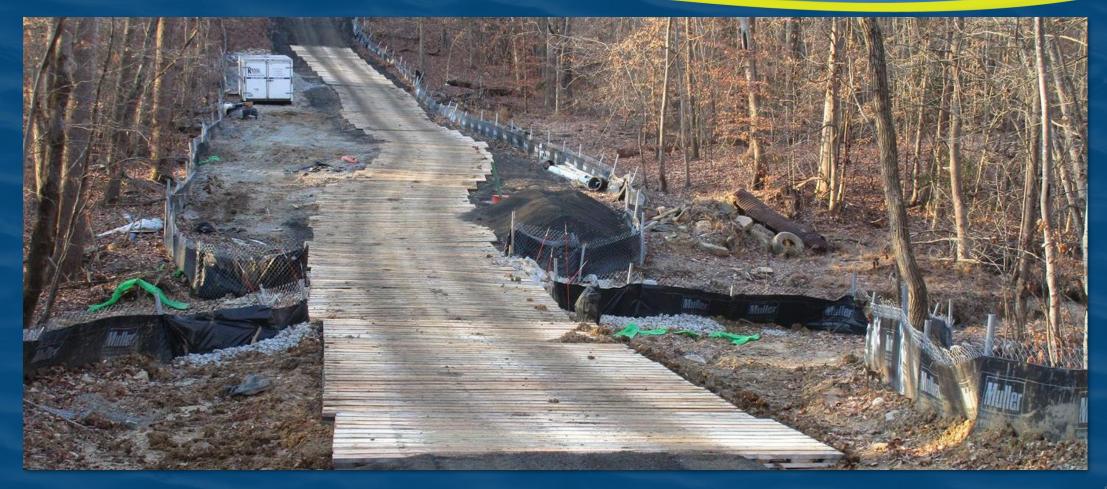



LIVE STREAM VIDEO



BPS – Slab on Grade





Access Road to Four Seasons Drive





Project Schedule and Status Update

Project Schedule.

- Notice to Proceed December 13, 2021.
- Total duration 949 calendar days to final completion.
- Construction commenced in the summer of 2022.
- On-site construction activities ongoing.
- Anticipated completion summer 2024.
- The project website is updated as status changes occur.
- Arcadis: Construction Manager / Project Representative
 On-site for the duration of the project.
- Service Authority Inspector on-site daily and as necessary.





SA Commitments

- To restore property affected by SA construction to an original or better condition.
- Road access shall be maintained at all times.
 - Emergency services, trash, mail, and other services.
- To continuously communicate and work with the Community Association concerning project status.
- Respond quickly to residents' concerns.
- Daily clean-up by the Design-Builder is required.



Questions and Contacts

 Project e-mail address Montclair_DB@pwcsa.org Project website https://www.pwcsa.org/montclair-db-project Service Authority Liaison David Scott **Project Manager** Phone: (703) 393-4474 Questions

Service Authority Exceptional Water Service

